PROJECT CHARTER, WORK BREAKDOWN STRUCTURE AND WBS DICTIONARY

ShopEase Online Store: Development of an E-commerce Web Application

Name : Abhay Maurya

PRN : 202301040187

Subject : Project Management (Assignment 1)

Project Domain : E-commerce Application

Document Version : 1.0, 07 Sep 2026

ABSTRACT

ShopEase is a family-owned clothing and lifestyle store in Pune with one physical shop, 15 employees and about 3,000 regular customers. Today most remote orders come through WhatsApp and Instagram messages and are written into an Excel sheet by hand. This causes wrong sizes and addresses, delayed payments and lost orders, and the business cannot grow beyond what the staff can handle on the phone.

This document defines the project that will give ShopEase its own e-commerce web application: a mobile-first online store with UPI and card payments, courier integration, GST invoices and an admin panel for products, stock and orders. The Project Charter records the business need, the business case, SMART objectives, scope boundaries, milestones, summary budget, environmental factors, risks, the authority given to the project manager and a stakeholder register with an engagement plan that is reviewed at every milestone.

The scope is then decomposed into a deliverable-oriented Work Breakdown Structure with 8 level-2 elements and 25 work packages. Each work package is described in the WBS Dictionary with its description, deliverables, acceptance criteria, exclusions, owner, schedule, effort and cost. The project runs for 25 weeks from 01 Sep 2026 with go-live on 27 Jan 2027, and has a total budget of Rs 11,70,800.

Keywords: Project Management, Project Charter, SMART Goals, Stakeholder Register, Work Breakdown Structure, WBS Dictionary, Scope Baseline, E-commerce.

1. INTRODUCTION

1.1 About the Organisation

ShopEase was started in 2014 by Mr. Rajesh Kulkarni and sells men's and women's casual wear, footwear and small home items. The shop has about 1,200 products (SKUs) from 8 regular suppliers. Sales were about Rs 1.9 crore in FY 2025-26. Since 2021 the business has also taken orders on WhatsApp and Instagram, which now make up about 35 orders a day and roughly a quarter of total sales.

1.2 Purpose of this Document

According to the PMBOK Guide, the project charter is the document that formally authorises a project and gives the project manager the authority to use organisational resources. The WBS breaks the total scope into smaller, manageable deliverables, and the WBS dictionary gives the detail of each element. Together with the scope statement, the WBS and WBS dictionary form the scope baseline against which the project is controlled.

1.3 Structure of the Document

Section 2 is the Project Charter. Section 3 is the stakeholder register and engagement plan. Section 4 explains how the WBS was built and shows it as a diagram and as an outline. Section 5 is the WBS Dictionary. Section 6 links the SMART goals to the work packages, and Section 7 concludes.

2. PROJECT CHARTER

2.1 Project Information

Project Title	ShopEase Online Store: E-commerce Web Application
Project Code	SE-ECOM-01
Organisation	ShopEase Retail, Kothrud, Pune
Project Sponsor	Mr. Rajesh Kulkarni, Owner
Project Manager	Abhay Maurya
Charter Date	07 Sep 2026
Planned Start / Go-live / Closure	01 Sep 2026 / 27 Jan 2027 / 16 Feb 2027
Total Budget	Rs 11,70,800 (including contingency and management reserve, see 2.9)
Project Type	New software product for an existing business; fixed date, fixed budget

Table 1: Project information

2.2 Business Need and Problem Statement

The current remote ordering process works as follows: a customer sends a photo of a product on WhatsApp, a staff member checks stock in the shop, confirms the price, asks for the address and a UPI screenshot, and writes the order into Excel. The order is packed and sent through a local courier. An internal check of 400 orders from June to August 2026 found:

- about 8% of orders had an error (wrong size, wrong item or wrong address), causing returns and re-shipping costs;
- about 15% of enquiries did not become orders because replies took more than 2 hours, especially in the evening;
- payments were checked manually from screenshots, and 11 orders in the period were shipped before payment was confirmed;
- two staff members spend most of their day on WhatsApp instead of serving walk-in customers;
- walk-in sales fell by about 12% compared with the previous year, while competitors and marketplaces sell the same type of products online.

The business need is therefore to **move remote ordering to a self-service online store** that takes payment before dispatch, removes manual order writing, and lets ShopEase sell to customers outside Pune without adding more staff.

2.3 Business Case

Item	Estimate	Basis
One-time project cost	Rs 11,70,800	Section 2.9
Running cost after launch	Rs 22,000 per month	Hosting, SMS/WhatsApp messages, support contract
Additional online sales	Rs 4,00,000 per month by month 6	About 15 new orders a day (customers outside Pune, evening orders) at Rs 900 average order value
Gross margin on additional sales	Rs 1,20,000 to 1,40,000 per month	30 to 35% gross margin on clothing
Savings	Rs 25,000 per month	Fewer returns from wrong orders and less staff time on WhatsApp
Net monthly benefit	Rs 1,23,000 to 1,43,000	Margin + savings - running cost
Payback period	about 12 months after go-live	Project cost / net monthly benefit, with sales growing over the first 6 months

Table 2: Summary business case

A marketplace-only option (selling on large marketplaces) was also considered. It was rejected as the main solution because of the 18 to 25% commission, no ownership of

customer data and no control over the brand, but it may be added later as a separate channel.

2.4 Project Objectives (SMART Goals)

The objectives are split into **project objectives**, which the project team delivers and which are measured at go-live or closure, and **business objectives**, which the sponsor owns and which are measured after the project because they depend on the business using the product.

ID	Specific	Measurable	Achievable	Relevant	Time-bound
G1	Launch the ShopEase online store (storefront and admin panel) with all Must-have features in the SRS	All 25 work packages accepted; site live on the ShopEase domain	25-week plan with 7 people; proven stack the team already uses	Solves the core business need of self-service ordering	Go-live 27 Jan 2027
G2	Complete the project within the approved cost baseline	Actual cost within Rs 11,19,800; variance reported weekly	Bottom-up estimates per work package plus 10% contingency	Owner is funding the project from savings; overrun is not affordable	Measured at closure, 16 Feb 2027
G3	Make the site fast on mobile phones	95% of pages load in under 3 s on 4G with 500 concurrent users	Cloud hosting in Mumbai, caching, image compression	Most customers order from Android phones	Load test in W17 to W19
G4	Launch with no serious quality or security problems	Zero open critical/high defects and VAPT findings; UAT pass rate at least 95%	Dedicated QA engineer and external audit are budgeted	Customer trust and payment safety	UAT sign-off by 18 Jan 2027
G5	Meet legal requirements for online selling in India	Checklist complete: GST invoices, DPDP consent and privacy notice, Consumer Protection (E-Commerce) Rules 2020 page details, no card data stored	Licensed gateway handles cards; CA checks invoices	Avoids penalties and gateway rejection	Checklist signed at go/no-go, W22
G6 (business)	Grow online orders through the website	Average of at least 50 website orders per day	Current 35 orders/day on WhatsApp move online, plus new customers outside Pune	Main source of the payback in 2.3	30 Apr 2027 (3 months after launch)

ID	Specific	Measurable	Achievable	Relevant	Time-bound
G7 (business)	Reduce order errors	Order error rate below 1% (from about 8%), from the admin dashboard	Customers choose size and address themselves; payment is confirmed automatically	Cuts return costs and complaints	30 Apr 2027

Table 3: SMART goals

2.5 High-Level Scope

In scope:

- Responsive customer website: catalogue, search and filters, OTP login and guest checkout, cart, coupons, checkout, order tracking, help pages.
- Online payment through a licensed gateway (UPI, cards, net banking, wallets) and Cash on Delivery for selected PIN codes.
- Courier aggregator integration for serviceability, labels and tracking; SMS, e-mail and WhatsApp order notifications.
- GST compliant invoices and a monthly export for the accountant.
- Admin panel: products, stock, orders, returns and refunds, and a sales dashboard.
- Hosting, CI/CD, security, backups and monitoring; testing including load test and external VAPT.
- Migration of the existing 1,200 products, staff training, go-live and two weeks of hypercare.

Out of scope (explicitly excluded so that they are not assumed to be included):

- Native Android and iOS apps.
- Selling on marketplaces (Amazon, Flipkart, Myntra) and multi-vendor features.
- Launch marketing and advertising (separate contract with the marketing agency).
- Replacing the Tally accounting software or the in-store billing machine.
- International shipping, loyalty points, gift cards, product reviews.
- Maintenance and new features after hypercare (separate annual maintenance contract).

2.6 Key Deliverables

1. Project management documents: charter, scope, schedule and cost baselines, status reports, closure report.
2. Requirements specification and approved UI/UX design.

3. Live e-commerce web application (storefront, payments, integrations and admin panel).
4. Hosting environments, CI/CD pipeline and backup and monitoring setup.
5. Test reports: functional, load test, VAPT and UAT sign-off.
6. Migrated product data, user manual and trained staff.

2.7 Summary Milestone Schedule

ID	Milestone	Planned date	Approved by
M1	Charter approved and kick-off held	07 Sep 2026	Sponsor
M2	Requirements and design signed off	14 Oct 2026	Sponsor, Operations Head
M3	Development feature complete (all Must-have stories on staging)	23 Dec 2026	Project Manager
M4	UAT signed off	18 Jan 2027	Sponsor
M5	Go-live of the online store	27 Jan 2027	Sponsor (go/no-go)
M6	Hypercare ends and project closed	16 Feb 2027	Sponsor

Table 4: Milestones

Work starts on 1 September 2026, right after the charter is approved. Go-live at the end of January puts the store online before the wedding season and Valentine's Day sales from February, and keeps development away from the shop's busiest time: during the Diwali week (week 11) store staff are not available for project work. The office holidays (Ganesh Chaturthi, Gandhi Jayanti, Dussehra, Diwali, Christmas, the year-end closure from 28 December to 1 January and Republic Day) are already included in the schedule.

2.8 Summary Budget

Level-2 WBS element	Effort (person-days)	Cost
1.1 Project Management	49	Rs 1,69,500
1.2 Requirements and Design	39	Rs 1,29,600
1.3 Customer Storefront	44	Rs 1,54,000
1.4 Payments and Integrations	22	Rs 76,500
1.5 Admin and Back Office	26	Rs 91,000
1.6 Infrastructure and Deployment	17	Rs 1,08,600
1.7 Testing and Quality	41	Rs 1,57,800
1.8 Launch and Transition	29	Rs 1,30,800
Work package total (labour Rs 8,97,800 + non-labour Rs 1,20,000)	**267**	**Rs 10,17,800**

Level-2 WBS element	Effort (person-days)	Cost
Contingency reserve (10%, controlled by PM for identified risks)		Rs 1,02,000
Cost baseline		**Rs 11,19,800**
Management reserve (5%, controlled by sponsor for unknown risks)		Rs 51,000
Total project budget		**Rs 11,70,800**

Table 5: Summary budget

Labour is estimated from person-days and the following daily rates: Project Manager Rs 3,500, Business Analyst Rs 3,000, UI/UX Designer Rs 3,000, Developer Rs 3,500, QA Engineer Rs 2,800 and DevOps Engineer Rs 3,800. Payment gateway, SMS and courier charges after launch are operating costs and are not part of the project budget.

2.9 Assumptions and Constraints

Assumptions	Constraints
• Payment gateway KYC is approved by week 13. • ShopEase provides product data, HSN codes and courier/WhatsApp accounts on time. • The owner and operations head can attend weekly reviews (1 hour). • The team of 7 is available for the full duration. • Customers already use UPI and are willing to order online.	• Budget is fixed at Rs 11,70,800. • Go-live must be before the wedding season sales from February. • Customer data must be stored in India. • No card data may be stored on ShopEase servers. • Staff have basic smartphone skills, so the admin panel must be very simple and partly in Marathi.

2.10 Enterprise Environmental Factors and Organisational Process Assets

These are the conditions outside the control of the project team that influence the project (EEFs), and the plans, processes and knowledge the organisation already has (OPAs).

Type	Factor	Effect on the project
Internal EEF	Small company (15 staff), no IT department	All technical work is done by the project team; a support contract is needed after launch
Internal EEF	Family-run culture; decisions taken by the owner	Fast approvals, but changes can come late; formal change control is needed
Internal EEF	Seasonal cash flow (Diwali and wedding season)	Payments to the team are linked to milestones

Type	Factor	Effect on the project
Internal EEF	Staff are new to software tools; some prefer Marathi	Simple admin screens, Marathi manual, hands-on training
External EEF	Digital Personal Data Protection Act 2023 and IT Act 2000	Consent, privacy notice, data security and storage in India
External EEF	Consumer Protection (E-Commerce) Rules 2020	Seller details, return policy, grievance officer and pricing shown on the site
External EEF	GST law (CGST/SGST/IGST, HSN codes)	Correct tax per delivery state on every invoice
External EEF	RBI rules for payment aggregators; UPI is the most used payment method	Only a licensed gateway is used; UPI must be the default option
External EEF	Strong competition from marketplaces and other local shops online	Fast launch and simple mobile experience are important
External EEF	Courier coverage differs by PIN code	Serviceability check before checkout; COD only where allowed
OPA	Excel product list and 5 years of sales records	Basis for data migration and for sales targets
OPA	Existing 7-day return and exchange policy, invoice format, supplier contracts	Reused in the returns workflow and invoices
OPA	PM's templates: charter, status report, risk register, change request	Used for project governance and reporting

Table 6: EEFs and OPAs

2.11 High-Level Risks

ID	Risk	Probability	Impact	Response
R1	Payment gateway KYC is delayed, blocking payment testing	Medium	High	Apply in week 3; keep a second gateway as backup; test in sandbox meanwhile
R2	Product data and photos are incomplete or late	High	Medium	Data template agreed in W3; photo shoot budgeted in 1.8.1; weekly data check
R3	Store staff resist the new process	Medium	Medium	Involve staff in requirements and UAT; Marathi training; show time saved
R4	Owner requests new features during development (scope creep)	High	High	Change control; MoSCoW priorities; Phase 2 backlog
R5	A developer leaves or falls ill	Low	High	Code reviews and documentation; both developers work on all modules

ID	Risk	Probability	Impact	Response
R6	Site slows down or fails at launch traffic	Low	High	Load test at 500 users; auto-scaling; launch campaign starts after site is stable
R7	Security breach or data leak	Low	High	VAPT, WAF, backups, no card data stored, least-privilege admin accounts

Table 7: High-level risks

2.12 Project Manager Authority Limits

The sponsor gives the project manager the following authority. Anything above these limits is escalated to the sponsor. The Change Control Board (CCB) is the sponsor, the operations head and the project manager.

Area	Project Manager can decide alone	Needs sponsor / CCB approval
Budget	Spend within approved work-package budgets; move up to Rs 25,000 between work packages; use contingency up to Rs 50,000 per risk event (sponsor informed in the weekly report)	Any use of the management reserve; any change to the cost baseline; single purchase above Rs 50,000
Schedule	Re-sequence activities and change internal dates as long as milestones do not move	Any milestone moving by more than 5 working days; any change to the go-live date
Scope	Small changes up to 2 person-days that do not affect a milestone or cost	All other changes, through a change request to the CCB
Team	Assign work, set priorities, approve leave of up to 2 days	Adding, replacing or releasing team members
Vendors	Collect quotes, evaluate and recommend vendors	Signing contracts and paying vendors (owner signs all contracts)
Technical	Choose tools, libraries and design details within the approved architecture	Changing the payment gateway, hosting provider or core technology stack
Quality	Stop a release to staging or production if a critical defect is open	Final go/no-go decision for go-live
Conflicts	Resolve conflicts inside the team	Conflicts between stakeholders that are not solved within 2 working days

Table 8: Project manager authority limits

2.13 Success and Exit Criteria

- Project objectives G1 to G5 are met and the sponsor signs the acceptance certificate.
- All deliverables in the WBS dictionary meet their acceptance criteria.
- Documents, source code, accounts and passwords are handed over to ShopEase.

- Business objectives G6 and G7 are measured by the sponsor on 30 April 2027 using the admin dashboard. They are not exit criteria for the project, but the result is reported in the benefits review.

The project may be stopped early if the payment gateway cannot be approved by week 15 with any provider, or if the forecast cost goes above the total budget, in which case the sponsor decides whether to continue.

2.14 Approval

Role	Name	Signature	Date
Project Sponsor	Rajesh Kulkarni		
Operations Head	Meera Kulkarni		
Project Manager	Abhay Maurya		

3. STAKEHOLDER REGISTER AND ENGAGEMENT PLAN

3.1 Identification and Assessment

Stakeholders were identified from the organisation chart, the current order process and the list of external partners. Power is the ability to influence decisions or stop the project; interest is how much the project affects the stakeholder. H = high, M = medium, L = low.

ID	Stakeholder	Role	Main interests / expectations	Influence on project	Power	Interest	Strategy
S01	Rajesh Kulkarni	Owner, Project Sponsor	Return on investment, launch before February, budget	Funds the project, final approvals	H	H	Manage closely
S02	Meera Kulkarni	Operations Head	Easier order handling, fewer errors, fair workload for staff	Approves requirements and UAT; CCB member	H	H	Manage closely
S03	Store and dispatch staff (6)	Daily users of admin panel	Fear of extra work and of being replaced; want simple screens	Can slow adoption after launch	L	H	Keep informed
S04	Accountant (external CA firm)	GST and accounting	Correct invoices and simple monthly data	Approves invoice format	M	L	Keep satisfied
S05	Abhay Maurya	Project Manager	Deliver on time, within budget and scope	Leads the team, reports to sponsor	H	H	Manage closely
S06	Project team	BA, UX, 2 developers, QA, DevOps	Clear requirements, realistic deadlines	Quality and speed of delivery	M	H	Manage closely

ID	Stakeholder	Role	Main interests / expectations	Influence on project	Power	Interest	Strategy
S07	Existing customers (about 3,000)	Future online buyers	Easy ordering, safe payment, fast delivery	Decide whether G6 is reached	L	H	Keep informed
S08	Payment gateway provider	Payment processing	Compliant merchant, complete KYC	Can block go-live (risk R1)	H	L	Keep satisfied
S09	Courier aggregator	Shipping and tracking	Order volume, correct API use	Delivery performance	M	L	Keep satisfied
S10	Cloud hosting provider	Servers and database	Paying customer	Uptime of the site	L	L	Monitor
S11	Government bodies (GST, data protection)	Regulation	Legal compliance	Penalties if rules are not met	H	L	Keep satisfied
S12	Clothing suppliers (8)	Product information	More sales of their products	Quality of product data and photos	L	M	Monitor
S13	Digital marketing agency	Launch campaign	Stable site and launch date	Brings traffic after go-live	L	M	Keep informed

Table 9: Stakeholder register: identification and assessment (version 1.0)

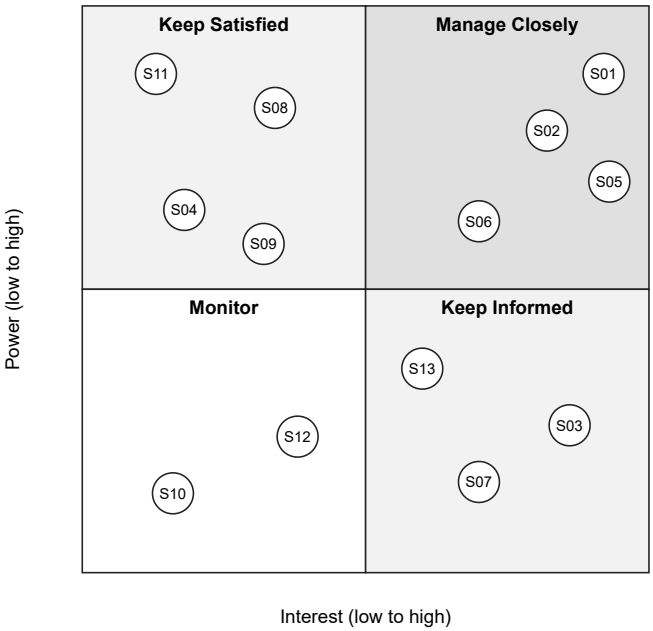


Figure 1: Power/interest grid of the stakeholders

3.2 Engagement Assessment Matrix

C is the current engagement level and D is the desired level by go-live. The gap between C and D decides how much effort is spent on each stakeholder.

ID	Stakeholder	Unaware	Resistant	Neutral	Supportive	Leading
S01	Rajesh Kulkarni				C	D
S02	Meera Kulkarni			C		D
S03	Store and dispatch staff (6)		C		D	
S04	Accountant (external CA firm)	C		D		
S05	Abhay Maurya					C, D
S06	Project team				C, D	
S07	Existing customers (about 3,000)	C			D	
S08	Payment gateway provider	C			D	
S09	Courier aggregator	C			D	
S10	Cloud hosting provider			C, D		
S11	Government bodies (GST, data protection)	C		D		
S12	Clothing suppliers (8)	C			D	
S13	Digital marketing agency			C	D	

Table 10: Engagement assessment matrix

3.3 Engagement Actions

ID	Engagement action	Frequency	Owner
S01	Weekly 1-hour review, milestone sign-offs, short WhatsApp update on Wednesdays	Weekly	PM
S02	Include in requirements workshops and UAT; CCB member; show how errors will be reduced	Weekly	PM
S03	Interview two staff in requirements; demo after each sprint in the shop; Marathi training; ask them to help in UAT	Every sprint (2 weeks)	BA
S04	Meeting in W3 for invoice rules; review of sample invoices in W16	At W3 and W16	BA
S06	Daily stand-up, sprint planning and review, recognise good work	Daily	PM
S07	Survey of 100 customers in W2; 5 customers test the prototype in W7; launch message from the shop	W2, W7, W22	BA
S08	Submit KYC documents in W3; weekly follow-up until approval	Weekly till approved	PM
S09	Account and API keys by W13; joint test of label printing	W13 to W15	DevOps
S10	Account and support plan set up in W6	Monthly	DevOps

ID	Engagement action	Frequency	Owner
S11	Compliance checklist reviewed by CA and PM before go-live	W22	PM
S12	Request product details and photos in W3 with the data template	Every 2 weeks till W16	BA
S13	Share launch date and staging link two weeks before go-live	W20 to W22	PM

Table 11: Stakeholder engagement actions

3.4 Keeping the Register Up to Date

The register is a living document. It is owned by the project manager and is stored with the version history in the project folder. It is updated:

- at every milestone review (M1 to M6), where power, interest and engagement level of each stakeholder are assessed again;
- when a new stakeholder appears (for example a new supplier or a second payment gateway);
- when a stakeholder's behaviour changes, for example a CCB member blocking a decision or staff complaints in a sprint demo;
- when a risk linked to a stakeholder occurs (R1 gateway, R3 staff).

Review point	What is checked again	Expected change
M1 kick-off (W2)	Full register created and agreed with the sponsor	Version 1.0 (this document)
M2 design sign-off (W7)	Staff reaction to prototype; gateway KYC status; supplier data response	S03 from Resistant to Neutral; S08 from Unaware to Neutral
M3 feature complete (W17)	Readiness of staff, accountant, courier for testing	S04, S09 to Neutral or Supportive; S13 added to weekly updates
M4 UAT sign-off (W21)	Users who will run the system every day	S02, S03 at desired level; otherwise extra training before go-live
M5 go-live (W22)	Customer feedback, complaints, order volume	S07 engagement measured through orders and feedback
M6 closure (W25)	Final record for lessons learned	Register archived with the project files

Table 12: Register review points

4. WORK BREAKDOWN STRUCTURE

4.1 Approach

The WBS was created top-down from the scope in Section 2.5 and then checked bottom-up with the team. The following rules were used:

- **Deliverable oriented:** level 2 elements are parts of the product (storefront, payments, admin panel and so on) plus project management, not phases. This makes it easy to check that every deliverable has an owner.
- **100% rule:** the work packages together contain all the work in the scope and nothing outside it. Work that is out of scope is written in the "Excludes" field of the dictionary.
- **Mutually exclusive:** no work appears in two work packages. For example, writing test cases is in 1.7.1, while fixing defects found in testing is also counted in 1.7.1 as developer effort, not in the feature work packages.
- **Size of work packages:** each work package has one owner, can be finished within about three weeks and can be estimated and checked on its own. Larger items were split, for example storefront into catalogue, accounts, checkout and tracking.
- **Coding:** 1.0 is the whole project, 1.x is level 2 (control accounts) and 1.x.y is level 3 (work packages).

4.2 WBS Diagram

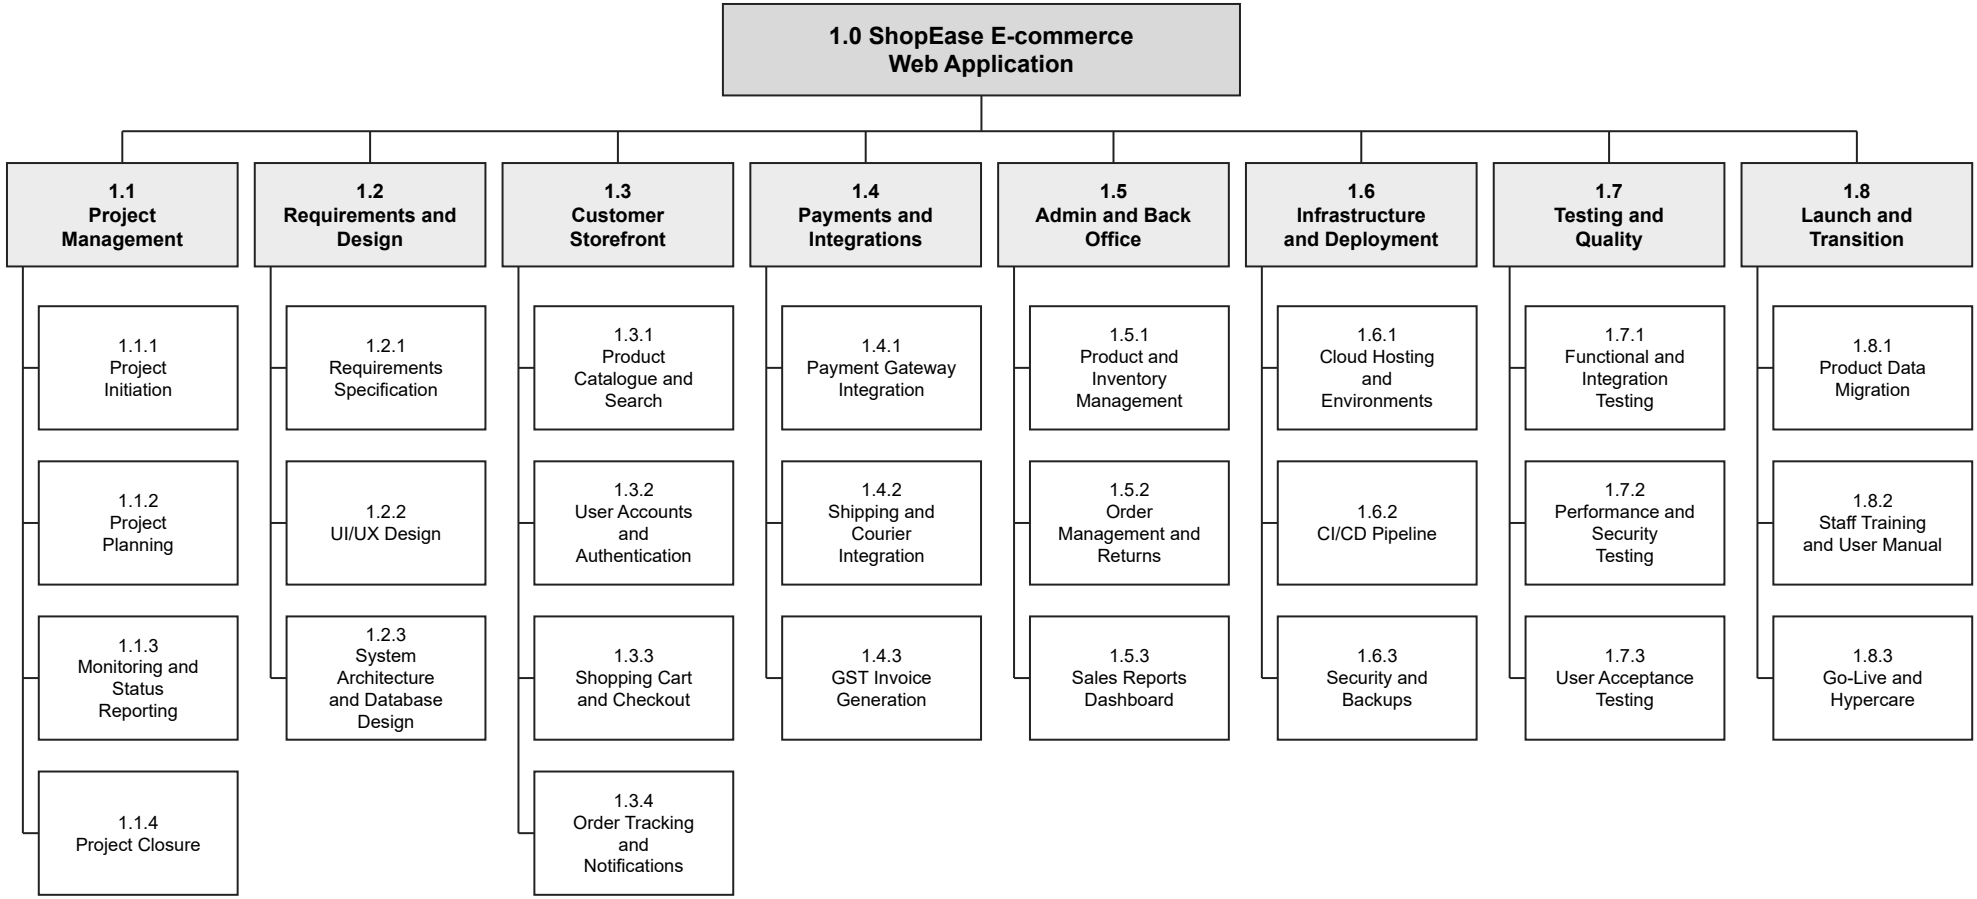


Figure 2: Work Breakdown Structure of the ShopEase e-commerce project (levels 1 to 3)

4.3 WBS Outline

Code	WBS element	Owner	Effort (p-days)	Cost
1.0	**ShopEase E-commerce Web Application**		**267**	**Rs 10,17,800**
1.1	**Project Management**		**49**	**Rs 1,69,500**
1.1.1	Project Initiation	PM	6	Rs 20,500
1.1.2	Project Planning	PM	8	Rs 27,000
1.1.3	Monitoring and Status Reporting	PM	30	Rs 1,05,000
1.1.4	Project Closure	PM	5	Rs 17,000
1.2	**Requirements and Design**		**39**	**Rs 1,29,600**
1.2.1	Requirements Specification	BA	12	Rs 37,000
1.2.2	UI/UX Design	UX	17	Rs 57,000
1.2.3	System Architecture and Database Design	DEV	10	Rs 35,600
1.3	**Customer Storefront**		**44**	**Rs 1,54,000**
1.3.1	Product Catalogue and Search	DEV	14	Rs 49,000
1.3.2	User Accounts and Authentication	DEV	8	Rs 28,000
1.3.3	Shopping Cart and Checkout	DEV	14	Rs 49,000
1.3.4	Order Tracking and Notifications	DEV	8	Rs 28,000
1.4	**Payments and Integrations**		**22**	**Rs 76,500**
1.4.1	Payment Gateway Integration	DEV	10	Rs 35,000
1.4.2	Shipping and Courier Integration	DEV	6	Rs 21,000
1.4.3	GST Invoice Generation	DEV	6	Rs 20,500
1.5	**Admin and Back Office**		**26**	**Rs 91,000**
1.5.1	Product and Inventory Management	DEV	10	Rs 35,000
1.5.2	Order Management and Returns	DEV	10	Rs 35,000
1.5.3	Sales Reports Dashboard	DEV	6	Rs 21,000
1.6	**Infrastructure and Deployment**		**17**	**Rs 1,08,600**
1.6.1	Cloud Hosting and Environments	OPS	6	Rs 58,800
1.6.2	CI/CD Pipeline	OPS	5	Rs 19,000
1.6.3	Security and Backups	OPS	6	Rs 30,800
1.7	**Testing and Quality**		**41**	**Rs 1,57,800**
1.7.1	Functional and Integration Testing	QA	22	Rs 64,400
1.7.2	Performance and Security Testing	QA	9	Rs 63,200
1.7.3	User Acceptance Testing	BA	10	Rs 30,200
1.8	**Launch and Transition**		**29**	**Rs 1,30,800**

Code	WBS element	Owner	Effort (p-days)	Cost
1.8.1	Product Data Migration	BA	9	Rs 58,500
1.8.2	Staff Training and User Manual	BA	5	Rs 20,000
1.8.3	Go-Live and Hypercare	PM	15	Rs 52,300

Table 13: WBS outline with effort and cost roll-up

Owner codes: PM = Project Manager, BA = Business Analyst, UX = UI/UX Designer, DEV = Full-stack Developers, QA = QA Engineer, OPS = DevOps Engineer.

5. WBS DICTIONARY

The WBS dictionary gives the details of every work package. Schedule weeks are project weeks; week 1 is the week starting Monday 31 Aug 2026, and work starts on Tuesday 01 Sep 2026. Cost is calculated from the effort and the daily rates in Section 2.8 plus any non-labour cost.

5.1 Summary

Code	Work package	Owner	Weeks	Effort	Cost
1.1.1	Project Initiation	PM	W1-W2	6	Rs 20,500
1.1.2	Project Planning	PM	W2-W3	8	Rs 27,000
1.1.3	Monitoring and Status Reporting	PM	W2-W24	30	Rs 1,05,000
1.1.4	Project Closure	PM	W24-W25	5	Rs 17,000
1.2.1	Requirements Specification	BA	W2-W4	12	Rs 37,000
1.2.2	UI/UX Design	UX	W4-W7	17	Rs 57,000
1.2.3	System Architecture and Database Design	DEV	W4-W6	10	Rs 35,600
1.3.1	Product Catalogue and Search	DEV	W7-W10	14	Rs 49,000
1.3.2	User Accounts and Authentication	DEV	W6-W8	8	Rs 28,000
1.3.3	Shopping Cart and Checkout	DEV	W10-W13	14	Rs 49,000
1.3.4	Order Tracking and Notifications	DEV	W16-W17	8	Rs 28,000
1.4.1	Payment Gateway Integration	DEV	W14-W15	10	Rs 35,000
1.4.2	Shipping and Courier Integration	DEV	W14-W15	6	Rs 21,000
1.4.3	GST Invoice Generation	DEV	W15-W16	6	Rs 20,500
1.5.1	Product and Inventory Management	DEV	W8-W10	10	Rs 35,000
1.5.2	Order Management and Returns	DEV	W12-W13	10	Rs 35,000
1.5.3	Sales Reports Dashboard	DEV	W16-W17	6	Rs 21,000
1.6.1	Cloud Hosting and Environments	OPS	W5-W6	6	Rs 58,800
1.6.2	CI/CD Pipeline	OPS	W6-W7	5	Rs 19,000

Code	Work package	Owner	Weeks	Effort	Cost
1.6.3	Security and Backups	OPS	W10-W12	6	Rs 30,800
1.7.1	Functional and Integration Testing	QA	W14-W19	22	Rs 64,400
1.7.2	Performance and Security Testing	QA	W17-W19	9	Rs 63,200
1.7.3	User Acceptance Testing	BA	W20-W21	10	Rs 30,200
1.8.1	Product Data Migration	BA	W14-W16	9	Rs 58,500
1.8.2	Staff Training and User Manual	BA	W20-W22	5	Rs 20,000
1.8.3	Go-Live and Hypercare	PM	W21-W24	15	Rs 52,300

Table 14: WBS dictionary summary

5.2 Work Package Details

1.1 Project Management

WBS Code	**1.1.1**
Work Package	**Project Initiation**
Control Account	1.1 Project Management
Owner	Project Manager (Abhay Maurya)
Description of Work	Prepare and get approval for the project charter, identify stakeholders and build the first version of the stakeholder register. Hold the kick-off meeting with the owner, the operations head and the team.
Deliverables	Approved project charter; stakeholder register v1.0; kick-off meeting minutes.
Acceptance Criteria	Charter signed by the sponsor (Mr. Rajesh Kulkarni). All 13 stakeholder groups listed with power, interest and engagement level.
Excludes	Detailed schedule and cost baseline (these are in 1.1.2).
Schedule	W1 to W2 (01 Sep to 07 Sep)
Predecessors	None
Resources and Effort	Project Manager 5 d, Business Analyst 1 d (total 6 person-days)
Cost Estimate	Rs 20,500 (labour Rs 20,500)
Assumptions / Constraints	Sponsor is available for at least two meetings in week 1.

WBS Code	**1.1.2**
Work Package	**Project Planning**
Control Account	1.1 Project Management
Owner	Project Manager (Abhay Maurya)
Description of Work	Create the scope baseline (scope statement, WBS and this WBS dictionary), the schedule with milestones, the cost baseline, the risk register and the communication plan.
Deliverables	Scope baseline; schedule baseline; cost baseline; risk register; communication plan.
Acceptance Criteria	Baselines reviewed and approved by the sponsor. Every work package has an owner, a cost estimate and dates.
Excludes	Day-to-day re-planning during execution (part of 1.1.3).
Schedule	W2 to W3 (08 Sep to 16 Sep)
Predecessors	1.1.1
Resources and Effort	Project Manager 6 d, Business Analyst 2 d (total 8 person-days)
Cost Estimate	Rs 27,000 (labour Rs 27,000)
Assumptions / Constraints	Requirements gathering runs in parallel; the WBS is refined once 1.2.1 is complete.

WBS Code	**1.1.3**
Work Package	**Monitoring and Status Reporting**
Control Account	1.1 Project Management
Owner	Project Manager (Abhay Maurya)
Description of Work	Track progress against the baselines, run the weekly status meeting, update the risk and stakeholder registers, run change control and send the weekly status report to the sponsor.
Deliverables	Weekly status reports (23); updated risk and stakeholder registers; change log; milestone review notes.
Acceptance Criteria	A status report is sent every Friday. Every change request is logged with a decision within 5 working days.
Excludes	Technical work of the team.
Schedule	W2 to W24 (08 Sep to 09 Feb)
Predecessors	1.1.2
Resources and Effort	Project Manager 30 d (total 30 person-days)
Cost Estimate	Rs 1,05,000 (labour Rs 1,05,000)
Assumptions / Constraints	The PM spends about 1.5 days per week on this work package.

WBS Code	**1.1.4**
Work Package	**Project Closure**
Control Account	1.1 Project Management
Owner	Project Manager (Abhay Maurya)
Description of Work	Get formal acceptance of the product, hand over documents and access, release the team, record lessons learned and close the vendor accounts that were opened for the project.
Deliverables	Signed acceptance certificate; lessons learned report; final project report; archived project files.
Acceptance Criteria	Sponsor signs the acceptance certificate. All credentials are transferred to ShopEase.
Excludes	Annual maintenance contract (separate agreement after the project).
Schedule	W24 to W25 (10 Feb to 16 Feb)
Predecessors	1.8.3
Resources and Effort	Project Manager 4 d, Business Analyst 1 d (total 5 person-days)
Cost Estimate	Rs 17,000 (labour Rs 17,000)
Assumptions / Constraints	Hypercare (1.8.3) has ended with no open critical defects.

1.2 Requirements and Design

WBS Code	**1.2.1**
Work Package	**Requirements Specification**
Control Account	1.2 Requirements and Design
Owner	Business Analyst
Description of Work	Interview the owner, operations head, store staff and the accountant, and study the current WhatsApp and Excel order process. Write the requirements as user stories with acceptance criteria and agree on priorities (MoSCoW).
Deliverables	Software Requirements Specification (SRS); prioritised product backlog; current and future process maps.
Acceptance Criteria	SRS signed off by the sponsor and operations head. Every Must-have story has acceptance criteria.
Excludes	Visual design of screens (1.2.2).
Schedule	W2 to W4 (08 Sep to 22 Sep)
Predecessors	1.1.1
Resources and Effort	Business Analyst 10 d, Project Manager 2 d (total 12 person-days)
Cost Estimate	Rs 37,000 (labour Rs 37,000)
Assumptions / Constraints	Store staff are available for two 1-hour interviews.

WBS Code	**1.2.2**
Work Package	**UI/UX Design**
Control Account	1.2 Requirements and Design
Owner	UI/UX Designer
Description of Work	Design a mobile-first storefront and a simple admin panel. Produce wireframes, then high fidelity mock-ups and a clickable prototype that is tested with 5 existing customers.
Deliverables	Wireframes; mock-ups for 18 screens; clickable prototype; style guide (colours, fonts, buttons); usability test notes.
Acceptance Criteria	Sponsor signs off the design (Milestone M2). At least 4 of 5 test customers complete a purchase in the prototype without help.
Excludes	Logo or brand redesign; marketing banners.
Schedule	W4 to W7 (23 Sep to 14 Oct)
Predecessors	1.2.1
Resources and Effort	UI/UX Designer 15 d, Business Analyst 2 d (total 17 person-days)
Cost Estimate	Rs 57,000 (labour Rs 51,000 + Rs 6,000 design tool licence)
Assumptions / Constraints	ShopEase supplies its existing logo and colours.

WBS Code	**1.2.3**
Work Package	**System Architecture and Database Design**
Control Account	1.2 Requirements and Design
Owner	Full-stack Developers (2)
Description of Work	Choose the technology stack, design the application architecture, the database schema (products, variants, customers, orders, payments, returns) and the API contracts used by the storefront and admin panel.
Deliverables	Architecture document; ER diagram and database schema; API specification.
Acceptance Criteria	Reviewed by the PM and DevOps engineer. Schema supports size and colour variants and GST rates per product.
Excludes	Hosting setup (1.6.1).
Schedule	W4 to W6 (21 Sep to 05 Oct)
Predecessors	1.2.1
Resources and Effort	Full-stack Developers (2) 8 d, DevOps Engineer 2 d (total 10 person-days)
Cost Estimate	Rs 35,600 (labour Rs 35,600)
Assumptions / Constraints	Stack: Node.js, React, PostgreSQL, Docker (team skills).

1.3 Customer Storefront

WBS Code	1.3.1
Work Package	**Product Catalogue and Search**
Control Account	1.3 Customer Storefront
Owner	Full-stack Developers (2)
Description of Work	Build the home page, category pages, product detail pages with size/colour variants and photos, and search with filters for category, price, size and availability.
Deliverables	Catalogue pages; product search with filters; responsive layouts for mobile and desktop.
Acceptance Criteria	Search returns results in under 1 second for 1,200 products. Out-of-stock variants cannot be added to cart.
Excludes	Product reviews and ratings (planned for a later phase).
Schedule	W7 to W10 (15 Oct to 04 Nov)
Predecessors	1.2.2, 1.2.3
Resources and Effort	Full-stack Developers (2) 14 d (total 14 person-days)
Cost Estimate	Rs 49,000 (labour Rs 49,000)
Assumptions / Constraints	Designs from 1.2.2 are final.

WBS Code	1.3.2
Work Package	**User Accounts and Authentication**
Control Account	1.3 Customer Storefront
Owner	Full-stack Developers (2)
Description of Work	Customer registration and login with mobile number and OTP, profile, saved addresses and order history. Guest checkout is also allowed.
Deliverables	Registration and OTP login; profile and address book; consent and privacy notice screens.
Acceptance Criteria	OTP login works on Android and iOS browsers. Passwords are not stored. Consent is recorded as required by the DPDP Act 2023.
Excludes	Social login (Google/Facebook).
Schedule	W6 to W8 (08 Oct to 19 Oct)
Predecessors	1.2.3
Resources and Effort	Full-stack Developers (2) 8 d (total 8 person-days)
Cost Estimate	Rs 28,000 (labour Rs 28,000)
Assumptions / Constraints	SMS OTP is sent through the gateway chosen in 1.2.3 at about Rs 0.20 per SMS (operating cost).

WBS Code	**1.3.3**
Work Package	**Shopping Cart and Checkout**
Control Account	1.3 Customer Storefront
Owner	Full-stack Developers (2)
Description of Work	Cart, coupon codes, delivery charge rules by PIN code, address selection and a single-page checkout that hands over to the payment gateway.
Deliverables	Cart; coupon engine; delivery charge rules; checkout flow.
Acceptance Criteria	A customer can go from cart to payment in 3 steps or fewer. Totals including GST and delivery charges match the test cases exactly.
Excludes	Loyalty points and gift cards.
Schedule	W10 to W13 (05 Nov to 27 Nov)
Predecessors	1.3.1, 1.3.2
Resources and Effort	Full-stack Developers (2) 14 d (total 14 person-days)
Cost Estimate	Rs 49,000 (labour Rs 49,000)
Assumptions / Constraints	Delivery is limited to PIN codes served by the courier partner.

WBS Code	**1.3.4**
Work Package	**Order Tracking and Notifications**
Control Account	1.3 Customer Storefront
Owner	Full-stack Developers (2)
Description of Work	Order status page for customers and automatic SMS, e-mail and WhatsApp messages at order placed, packed, shipped, delivered and refunded.
Deliverables	Order tracking page; notification templates; notification service.
Acceptance Criteria	Each status change sends the correct message within 2 minutes in all test cases.
Excludes	Marketing or promotional messages.
Schedule	W16 to W17 (14 Dec to 23 Dec)
Predecessors	1.3.3, 1.4.2
Resources and Effort	Full-stack Developers (2) 8 d (total 8 person-days)
Cost Estimate	Rs 28,000 (labour Rs 28,000)
Assumptions / Constraints	WhatsApp Business API account is approved by week 15.

1.4 Payments and Integrations

WBS Code	1.4.1
Work Package	**Payment Gateway Integration**
Control Account	1.4 Payments and Integrations
Owner	Full-stack Developers (2)
Description of Work	Integrate a licensed payment gateway for UPI, cards, net banking and wallets, plus Cash on Delivery for selected PIN codes. Handle success, failure, refunds and webhook reconciliation.
Deliverables	Payment integration; refund flow; daily settlement reconciliation report.
Acceptance Criteria	All payment methods pass in gateway test mode and with one real Rs 1 transaction each. No card data is stored on ShopEase servers.
Excludes	Selecting or negotiating the gateway contract (done by the sponsor in week 3).
Schedule	W14 to W15 (30 Nov to 11 Dec)
Predecessors	1.3.3 (partial)
Resources and Effort	Full-stack Developers (2) 10 d (total 10 person-days)
Cost Estimate	Rs 35,000 (labour Rs 35,000)
Assumptions / Constraints	Gateway KYC for ShopEase is approved before week 14 (risk R1).

WBS Code	1.4.2
Work Package	**Shipping and Courier Integration**
Control Account	1.4 Payments and Integrations
Owner	Full-stack Developers (2)
Description of Work	Connect to the courier aggregator API to check PIN code serviceability, create shipments, print labels and fetch tracking status.
Deliverables	Courier API integration; shipping label printing; tracking status updates.
Acceptance Criteria	A label is generated for a test order in under 30 seconds and tracking status updates automatically.
Excludes	Own delivery fleet or same-day delivery.
Schedule	W14 to W15 (30 Nov to 07 Dec)
Predecessors	1.5.2 (partial)
Resources and Effort	Full-stack Developers (2) 6 d (total 6 person-days)
Cost Estimate	Rs 21,000 (labour Rs 21,000)
Assumptions / Constraints	Courier aggregator account and API keys are provided by ShopEase by week 13.

WBS Code	**1.4.3**
Work Package	**GST Invoice Generation**
Control Account	1.4 Payments and Integrations
Owner	Full-stack Developers (2)
Description of Work	Generate GST compliant invoices (CGST/SGST or IGST by delivery state, HSN codes) as PDF for every order and export a monthly sales file for the accountant.
Deliverables	Invoice generator; monthly GST sales export in Excel format.
Acceptance Criteria	Accountant (CA firm) checks 20 sample invoices and confirms they are correct.
Excludes	Filing GST returns; replacing the Tally accounting software.
Schedule	W15 to W16 (08 Dec to 14 Dec)
Predecessors	1.2.3
Resources and Effort	Full-stack Developers (2) 5 d, Business Analyst 1 d (total 6 person-days)
Cost Estimate	Rs 20,500 (labour Rs 20,500)
Assumptions / Constraints	HSN codes and GST rates for all products are supplied by the accountant.

1.5 Admin and Back Office

WBS Code	**1.5.1**
Work Package	**Product and Inventory Management**
Control Account	1.5 Admin and Back Office
Owner	Full-stack Developers (2)
Description of Work	Admin screens to add and edit products, variants, prices, photos and stock, bulk upload from Excel and low-stock alerts. Stock is shared between the website and the physical store.
Deliverables	Product admin; Excel bulk upload; stock management with low-stock alerts.
Acceptance Criteria	Staff can add a product with 3 variants in under 5 minutes after training. Bulk upload of 1,200 rows completes without errors.
Excludes	Integration with the in-store billing machine (store stock is updated through the admin panel).
Schedule	W8 to W10 (21 Oct to 03 Nov)
Predecessors	1.2.3
Resources and Effort	Full-stack Developers (2) 10 d (total 10 person-days)
Cost Estimate	Rs 35,000 (labour Rs 35,000)
Assumptions / Constraints	Product data template is agreed in 1.2.1.

WBS Code	**1.5.2**
Work Package	**Order Management and Returns**
Control Account	1.5 Admin and Back Office
Owner	Full-stack Developers (2)
Description of Work	Admin screens to view, filter and process orders (confirm, pack, ship, cancel), handle returns and exchanges within the 7-day return policy and trigger refunds.
Deliverables	Order management screens; returns and exchange workflow; refund trigger.
Acceptance Criteria	Operations staff process a complete order and a return in the test system without developer help.
Excludes	Warehouse management system or barcode scanners.
Schedule	W12 to W13 (16 Nov to 27 Nov)
Predecessors	1.3.3
Resources and Effort	Full-stack Developers (2) 10 d (total 10 person-days)
Cost Estimate	Rs 35,000 (labour Rs 35,000)
Assumptions / Constraints	Return policy is the existing 7-day store policy.

WBS Code	**1.5.3**
Work Package	**Sales Reports Dashboard**
Control Account	1.5 Admin and Back Office
Owner	Full-stack Developers (2)
Description of Work	Dashboard for the owner with daily orders, revenue, average order value, top products, payment method split and order error rate.
Deliverables	Reports dashboard; CSV export of all reports.
Acceptance Criteria	Figures match a manual calculation on the test data set. Dashboard loads in under 3 seconds.
Excludes	Advanced analytics or forecasting.
Schedule	W16 to W17 (15 Dec to 22 Dec)
Predecessors	1.5.2
Resources and Effort	Full-stack Developers (2) 6 d (total 6 person-days)
Cost Estimate	Rs 21,000 (labour Rs 21,000)
Assumptions / Constraints	Order error rate is defined in 1.2.1 (wrong item, size or address).

1.6 Infrastructure and Deployment

WBS Code	**1.6.1**
Work Package	**Cloud Hosting and Environments**
Control Account	1.6 Infrastructure and Deployment
Owner	DevOps Engineer
Description of Work	Set up development, staging and production environments on a cloud provider (Mumbai region), with Docker containers, a managed PostgreSQL database, domain and SSL certificate.
Deliverables	Three environments; domain and SSL; environment documentation.
Acceptance Criteria	Staging and production are reachable over HTTPS. Data is stored in India.
Excludes	Hosting cost after hypercare (operating cost paid by ShopEase).
Schedule	W5 to W6 (30 Sep to 09 Oct)
Predecessors	1.2.3
Resources and Effort	DevOps Engineer 6 d (total 6 person-days)
Cost Estimate	Rs 58,800 (labour Rs 22,800 + Rs 36,000 cloud hosting for 6 months, domain and SSL)
Assumptions / Constraints	Cloud account is opened in the name of ShopEase.

WBS Code	**1.6.2**
Work Package	**CI/CD Pipeline**
Control Account	1.6 Infrastructure and Deployment
Owner	DevOps Engineer
Description of Work	Pipeline that runs automated tests on every commit, builds Docker images and deploys to staging automatically and to production after manual approval.
Deliverables	CI/CD pipeline; deployment runbook; rollback procedure.
Acceptance Criteria	A commit reaches staging in under 15 minutes. A rollback to the previous version is shown to the PM.
Excludes	Mobile app build pipelines.
Schedule	W6 to W7 (06 Oct to 12 Oct)
Predecessors	1.6.1
Resources and Effort	DevOps Engineer 5 d (total 5 person-days)
Cost Estimate	Rs 19,000 (labour Rs 19,000)
Assumptions / Constraints	Code is kept in a private GitHub repository owned by ShopEase.

WBS Code	**1.6.3**
Work Package	**Security and Backups**
Control Account	1.6 Infrastructure and Deployment
Owner	DevOps Engineer
Description of Work	Harden the servers, configure the web application firewall, rate limiting and HTTPS-only access, set up daily database backups with a tested restore, monitoring and alerts.
Deliverables	Security configuration; daily backups with restore test; uptime monitoring and alerts.
Acceptance Criteria	Restore from backup completed in under 1 hour in a test. Alerts reach the DevOps engineer and PM.
Excludes	Third-party security audit (1.7.2).
Schedule	W10 to W12 (04 Nov to 20 Nov)
Predecessors	1.6.1
Resources and Effort	DevOps Engineer 6 d (total 6 person-days)
Cost Estimate	Rs 30,800 (labour Rs 22,800 + Rs 8,000 backup storage)
Assumptions / Constraints	Backups are kept for 30 days.

1.7 Testing and Quality

WBS Code	**1.7.1**
Work Package	**Functional and Integration Testing**
Control Account	1.7 Testing and Quality
Owner	QA Engineer
Description of Work	Write and run test cases for every user story, regression tests after each sprint and end-to-end tests of order, payment, shipping and refund flows. Developers fix the defects found.
Deliverables	Test plan; about 250 test cases; defect log; test summary report.
Acceptance Criteria	100% of Must-have stories tested. No open critical or high defects at the end of week 19.
Excludes	Testing of third-party systems themselves (gateway, courier).
Schedule	W14 to W19 (02 Dec to 06 Jan)
Predecessors	1.3.x, 1.4.x, 1.5.x (feature complete by W17)
Resources and Effort	QA Engineer 18 d, Full-stack Developers (2) 4 d (total 22 person-days)
Cost Estimate	Rs 64,400 (labour Rs 64,400)
Assumptions / Constraints	Test data from 1.8.1 is available by week 16.

WBS Code	**1.7.2**
Work Package	**Performance and Security Testing**
Control Account	1.7 Testing and Quality
Owner	QA Engineer
Description of Work	Load test the site with 500 concurrent users and get an external vulnerability assessment and penetration test (VAPT). Fix and retest the findings.
Deliverables	Load test report; VAPT report; retest report.
Acceptance Criteria	95% of pages load in under 3 seconds at 500 concurrent users. No open critical or high VAPT findings.
Excludes	Ongoing yearly security audits.
Schedule	W17 to W19 (22 Dec to 08 Jan)
Predecessors	1.6.3, 1.7.1
Resources and Effort	QA Engineer 6 d, DevOps Engineer 3 d (total 9 person-days)
Cost Estimate	Rs 63,200 (labour Rs 28,200 + Rs 35,000 external security audit (VAPT))
Assumptions / Constraints	Audit firm is booked by week 15.

WBS Code	**1.7.3**
Work Package	**User Acceptance Testing**
Control Account	1.7 Testing and Quality
Owner	Business Analyst
Description of Work	The owner, operations head and two store staff run the agreed UAT scripts on staging with real product data and record results.
Deliverables	UAT scripts; UAT results; UAT sign-off (Milestone M4).
Acceptance Criteria	At least 95% of UAT scripts pass and the sponsor signs the UAT sign-off.
Excludes	New features requested during UAT (handled through change control).
Schedule	W20 to W21 (11 Jan to 18 Jan)
Predecessors	1.7.1, 1.7.2, 1.8.1
Resources and Effort	QA Engineer 4 d, Business Analyst 4 d, Project Manager 2 d (total 10 person-days)
Cost Estimate	Rs 30,200 (labour Rs 30,200)
Assumptions / Constraints	Users are available for 3 half days in week 20.

1.8 Launch and Transition

WBS Code	**1.8.1**
Work Package	**Product Data Migration**
Control Account	1.8 Launch and Transition
Owner	Business Analyst
Description of Work	Clean the existing Excel product list (about 1,200 SKUs), add missing details and photos, and import it into production through the bulk upload.
Deliverables	Cleaned product master file; product photos; import log.
Acceptance Criteria	All 1,200 SKUs are live with price, stock, HSN code and at least one photo. A sample of 50 is checked by the operations head.
Excludes	Migrating old WhatsApp order history.
Schedule	W14 to W16 (30 Nov to 15 Dec)
Predecessors	1.5.1
Resources and Effort	Business Analyst 6 d, Full-stack Developers (2) 3 d (total 9 person-days)
Cost Estimate	Rs 58,500 (labour Rs 28,500 + Rs 30,000 photo shoot for about 300 products without photos)
Assumptions / Constraints	Operations staff help with checking sizes and stock counts.

WBS Code	**1.8.2**
Work Package	**Staff Training and User Manual**
Control Account	1.8 Launch and Transition
Owner	Business Analyst
Description of Work	Train the owner and 6 store and dispatch staff on product, order and returns handling. Prepare a simple illustrated user manual in English and Marathi.
Deliverables	Training sessions (2); user manual; quick reference card for dispatch.
Acceptance Criteria	Every trained user processes an order and a return on their own in the training test.
Excludes	Training of customers (help pages are part of 1.3.1).
Schedule	W20 to W22 (14 Jan to 25 Jan)
Predecessors	1.7.3
Resources and Effort	Business Analyst 5 d (total 5 person-days)
Cost Estimate	Rs 20,000 (labour Rs 15,000 + Rs 5,000 printed manuals and training session)
Assumptions / Constraints	Staff are released for two 2-hour sessions.

WBS Code	**1.8.3**
Work Package	**Go-Live and Hypercare**
Control Account	1.8 Launch and Transition
Owner	Project Manager (Abhay Maurya)
Description of Work	Go/no-go meeting, production deployment on Wednesday 27 January 2027, two weeks of hypercare with daily checks and quick fixes, and handover of support to ShopEase.
Deliverables	Go/no-go checklist; live website (Milestone M5); hypercare log; support handover note.
Acceptance Criteria	Site is live with no critical defect open for 5 continuous working days during hypercare.
Excludes	New features after go-live.
Schedule	W21 to W24 (20 Jan to 09 Feb)
Predecessors	1.7.3, 1.8.1, 1.8.2
Resources and Effort	Full-stack Developers (2) 6 d, DevOps Engineer 4 d, QA Engineer 2 d, Project Manager 3 d (total 15 person-days)
Cost Estimate	Rs 52,300 (labour Rs 52,300)
Assumptions / Constraints	Launch marketing is run separately by the agency from 27 January.

6. TRACEABILITY FROM GOALS TO WORK PACKAGES

Each SMART goal in the charter is supported by at least one work package, and every work package supports at least one goal. This check confirms that the WBS covers the purpose of the project and does not contain unnecessary work.

SMART goal	Supported by work packages
G1 Launch with all Must-have features	1.2.1, 1.2.2, 1.3.1 to 1.3.4, 1.4.1 to 1.4.3, 1.5.1 to 1.5.3, 1.8.3
G2 Within cost baseline	1.1.2 (cost baseline), 1.1.3 (weekly cost tracking and change control)
G3 Fast on mobile	1.2.2 (mobile-first design), 1.2.3, 1.6.1, 1.7.2 (load test)
G4 No serious defects or security issues	1.6.3, 1.7.1, 1.7.2 (VAPT), 1.7.3 (UAT)
G5 Legal compliance	1.3.2 (DPDP consent), 1.4.1 (no card data), 1.4.3 (GST invoices), 1.3.1 (seller and policy pages)
G6 50 website orders per day	1.3.1, 1.3.3 (easy checkout), 1.8.1 (full catalogue), 1.5.3 (measurement)
G7 Order error rate below 1%	1.3.3 (customer selects size and address), 1.4.1 (auto payment check), 1.5.2, 1.8.2 (training), 1.5.3 (measurement)

Table 15: Goal to work package traceability

6.1 Scope Boundaries in Practice

Some requests are likely to come up during the project. The table shows how the charter and WBS are used to answer them.

Likely request	Where it stands	Action
"Can we also have an Android app?"	Out of scope (2.5)	Recorded for Phase 2; the website is mobile-first
"Show product reviews and ratings"	Excluded in 1.3.1	Change request to CCB; estimated 6 person-days
"Add a festival discount banner"	Inside 1.3.3 (coupons) and admin content	No change needed
"Connect the in-store billing machine"	Excluded in 1.5.1	Change request; needs vendor API, likely Phase 2
"Run Instagram ads at launch"	Out of scope (marketing agency)	Coordinate dates through S13

Table 16: Handling of scope requests

7. CONCLUSION

This document authorises the ShopEase online store project and gives a clear baseline for its scope. The charter explains why the project is needed, with figures from the current WhatsApp order process, and sets seven SMART goals, five for the project and two for the business. It defines what is in and out of scope, the milestones up to go-live on 27 Jan 2027, a budget of Rs 11,70,800 with reserves, the environmental factors that affect a small Indian retailer selling online, the key risks and the exact limits of the project manager's authority.

The stakeholder register shows that the biggest engagement gaps are with the store staff and the operations head, so most engagement effort goes to them, and it is reviewed again at every milestone. The WBS divides the scope into 8 deliverable-oriented elements and 25 work packages, and the WBS dictionary describes each work package with deliverables, acceptance criteria, exclusions, schedule, effort and cost. The cost roll-up of the WBS matches the budget in the charter, and the traceability table shows that every goal is covered by the work.

REFERENCES

1. Project Management Institute. A Guide to the Project Management Body of Knowledge (PMBOK Guide), 7th Edition, 2021.
2. Project Management Institute. Practice Standard for Work Breakdown Structures, 3rd Edition, 2019.
3. Project Management Institute. Process Groups: A Practice Guide, 2022.
4. Schwalbe, K. Information Technology Project Management, 9th Edition, Cengage, 2019.

5. Doran, G. T. There's a S.M.A.R.T. way to write management's goals and objectives. Management Review, 70(11), 1981.
6. Government of India. The Digital Personal Data Protection Act, 2023.
7. Government of India. Consumer Protection (E-Commerce) Rules, 2020.
8. Reserve Bank of India. Guidelines on Regulation of Payment Aggregators and Payment Gateways, 2020.
9. Central Board of Indirect Taxes and Customs. GST Invoice Rules. Available at: https://cbic-gst.gov.in
